

WIS 20 Interchange

News & Updates



94 NORTH-SOUTH
FREEWAY PROJECT

Last Updated: May 22, 2015

We're Open!


Questions, comments, concerns?
Come and visit us!

WIS 20 Project Field Office

1520 S. Sylvania Avenue, Suite 316
Sturtevant, WI

Cynthia De Vor

Public Involvement Leader
(262) 510-8901

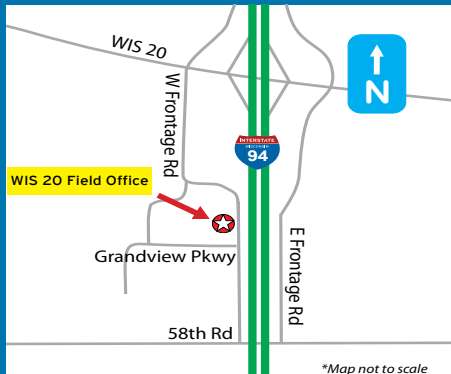

Greetings from the Wisconsin Department of Transportation!

Listed below are construction activities for the WIS 20 reconstruction project over the next few weeks:

Late May through mid-June, 2015:

- Continuation of mainline grading and storm sewer work
- Completion of retaining wall at south abutment at WIS 20
- I-94 mainline concrete paving operations scheduled to begin early June
- Concrete pour of south abutment structure, pier footings, column stems are also scheduled to begin early June
- Mill and overlay of County K exit ramp from I-94 EAST (SB) is scheduled for early June
 - Paving operations will require nighttime closures of the County K exit ramp (to be announced)

In observation of the upcoming holiday, and in the interest of traffic safety, construction activities will be halted over the upcoming holiday weekend.

All work is weather dependent and subject to change.

Plan Ahead, Drive Safely, Move Forward



U.S. Department of Transportation
Federal Highway
Administration



Find us online at:
Plan94.org



Find us on Facebook at:
Wisconsin Plan 94



Find us on Twitter at:
@WisconsinPlan94
